
Group 10: project Gantt, Oct 1 to Dec 12, 2026


Each row is a phase; its bars are its tasks by status; n/N at the right = tasks done; a page per track with a bar per task: gantt.pdf. Generated by tools/make_gantt.py on 2026-11-04 from e498341.

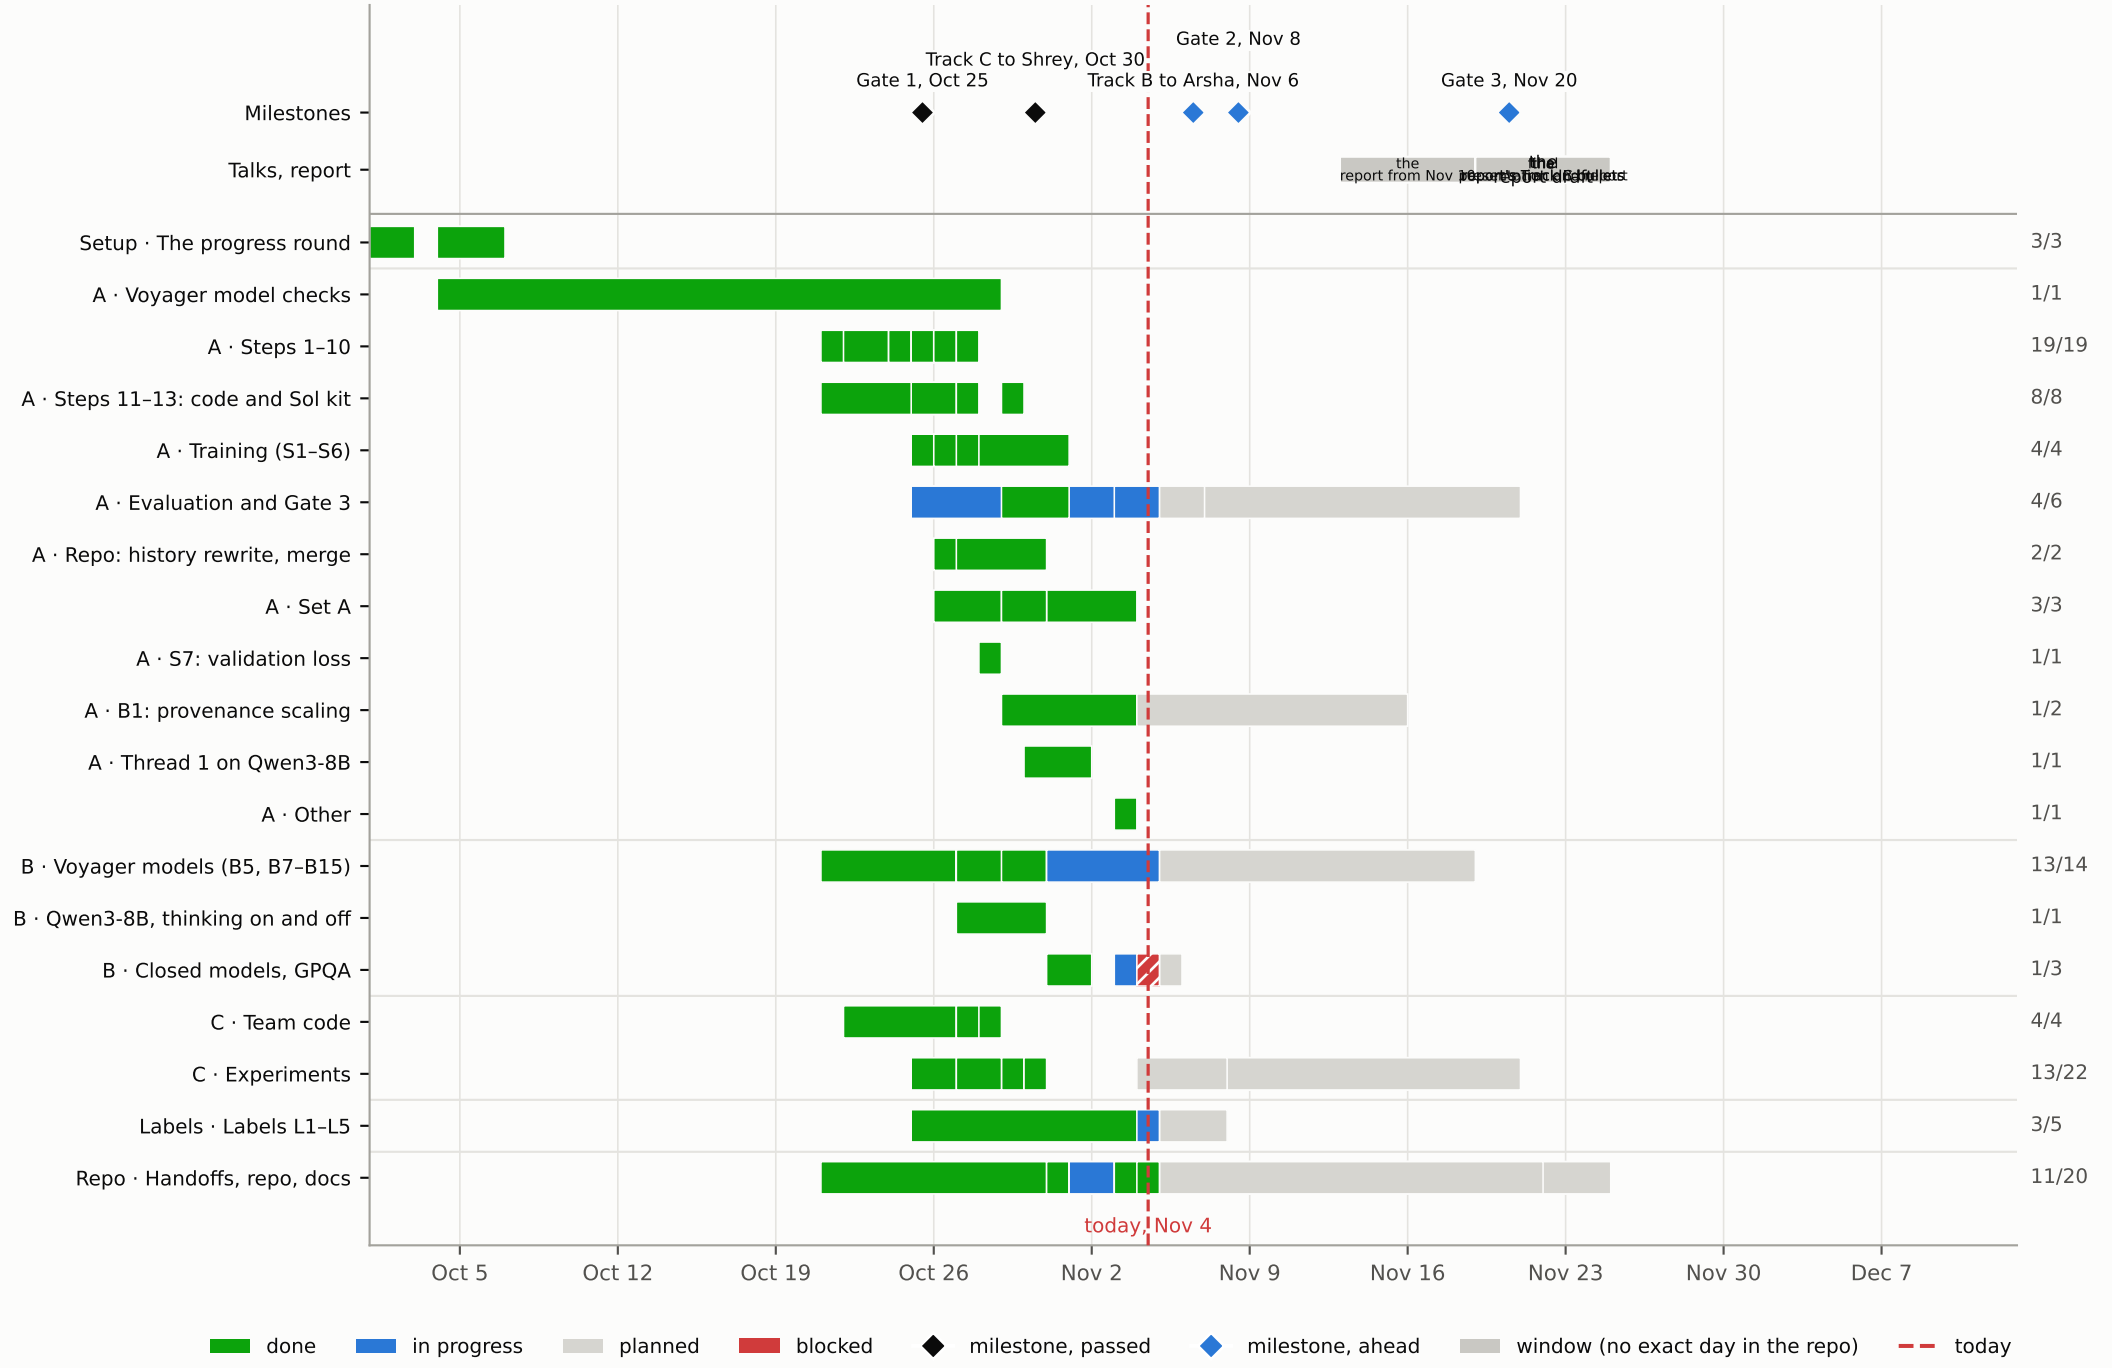

Track A: explain and fix

35 of 38 tasks done (92%). Owner: Ritik.

A bar per task, by status; * = an inferred date (the Gantt sheet's Date basis says from what); dotted lines: gates and handoffs; shaded: the report and presentation windows.

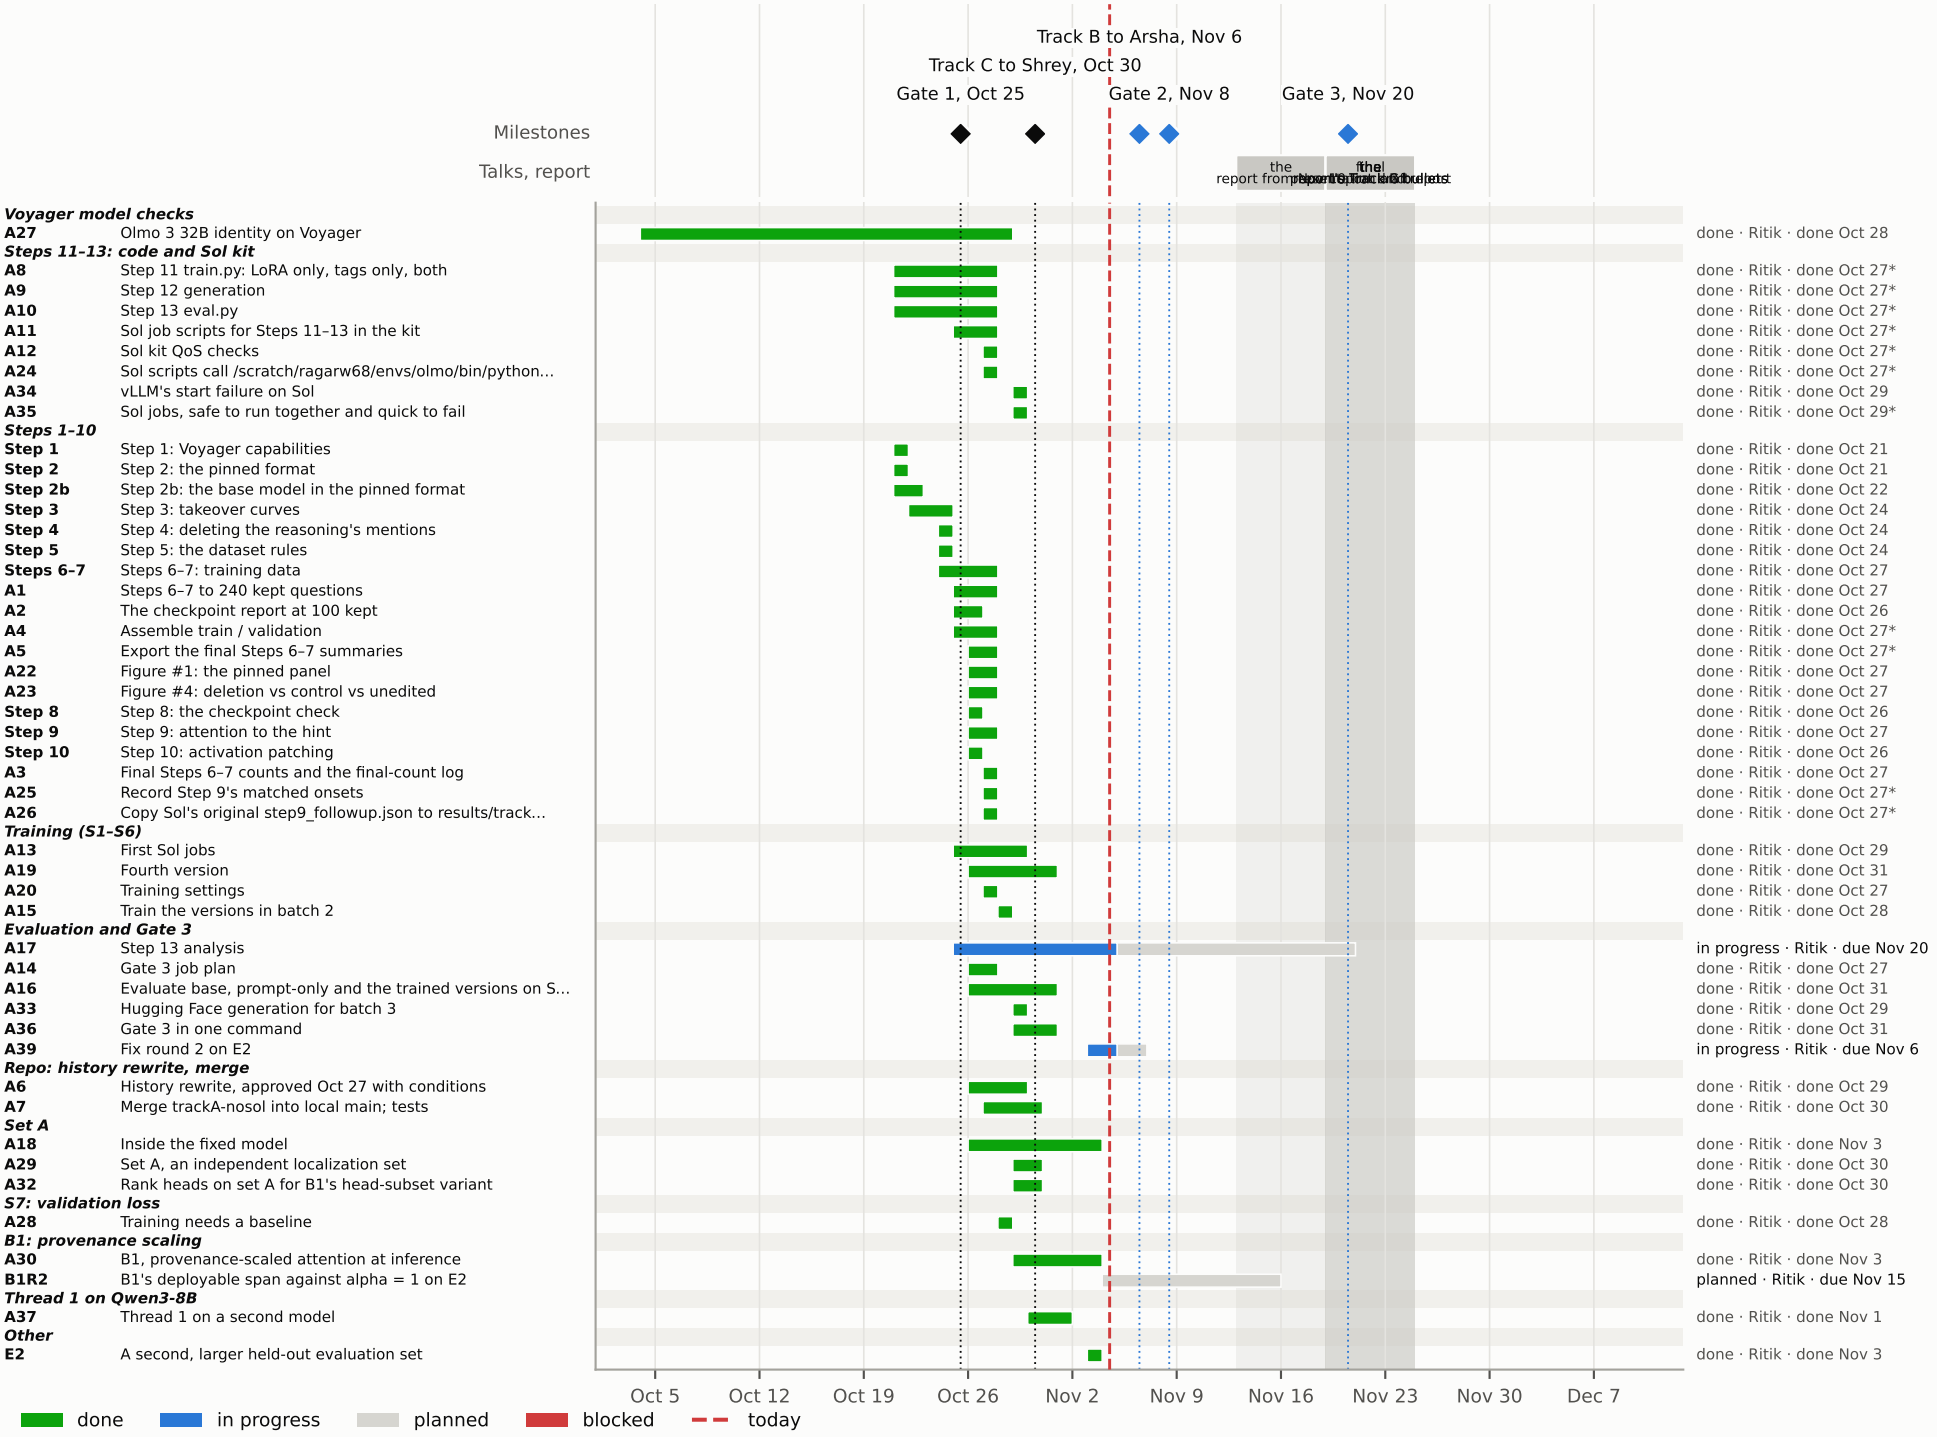


Voyager model checks		
A27	Olmo 3 32B identity on Voyager	done · Ritik · done Oct 28
Steps 11–13: code and Sol kit		
A8	Step 11 train.py: LoRA only, tags only, both	done · Ritik · done Oct 27*
A9	Step 12 generation	done · Ritik · done Oct 27*
A10	Step 13 eval.py	done · Ritik · done Oct 27*
A11	Sol job scripts for Steps 11–13 in the kit	done · Ritik · done Oct 27*
A12	Sol kit QoS checks	done · Ritik · done Oct 27*
A24	Sol scripts call /scratch/ragarw68/envs/olmo/bin/python...	done · Ritik · done Oct 27*
A34	vLLM's start failure on Sol	done · Ritik · done Oct 29
A35	Sol jobs, safe to run together and quick to fail	done · Ritik · done Oct 29*
Steps 1–10		
Step 1	Step 1: Voyager capabilities	done · Ritik · done Oct 21
Step 2	Step 2: the pinned format	done · Ritik · done Oct 21
Step 2b	Step 2b: the base model in the pinned format	done · Ritik · done Oct 22
Step 3	Step 3: takeover curves	done · Ritik · done Oct 24
Step 4	Step 4: deleting the reasoning's mentions	done · Ritik · done Oct 24
Step 5	Step 5: the dataset rules	done · Ritik · done Oct 24
Steps 6–7	Steps 6–7: training data	done · Ritik · done Oct 27
A1	Steps 6–7 to 240 kept questions	done · Ritik · done Oct 27
A2	The checkpoint report at 100 kept	done · Ritik · done Oct 26
A4	Assemble train / validation	done · Ritik · done Oct 27*
A5	Export the final Steps 6–7 summaries	done · Ritik · done Oct 27*
A22	Figure #1: the pinned panel	done · Ritik · done Oct 27
A23	Figure #4: deletion vs control vs unedited	done · Ritik · done Oct 27
Step 8	Step 8: the checkpoint check	done · Ritik · done Oct 26
Step 9	Step 9: attention to the hint	done · Ritik · done Oct 27
Step 10	Step 10: activation patching	done · Ritik · done Oct 26
A3	Final Steps 6–7 counts and the final-count log	done · Ritik · done Oct 27
A25	Record Step 9's matched onsets	done · Ritik · done Oct 27*
A26	Copy Sol's original step9_followup.json to results/track...	done · Ritik · done Oct 27*
Training (S1–S6)		
A13	First Sol jobs	done · Ritik · done Oct 29
A19	Fourth version	done · Ritik · done Oct 31
A20	Training settings	done · Ritik · done Oct 27
A15	Train the versions in batch 2	done · Ritik · done Oct 28
Evaluation and Gate 3		
A17	Step 13 analysis	in progress · Ritik · due Nov 20
A14	Gate 3 job plan	done · Ritik · done Oct 27
A16	Evaluate base, prompt-only and the trained versions on S...	done · Ritik · done Oct 31
A33	Hugging Face generation for batch 3	done · Ritik · done Oct 29
A36	Gate 3 in one command	done · Ritik · done Oct 31
A39	Fix round 2 on E2	in progress · Ritik · due Nov 6
Repo: history rewrite, merge		
A6	History rewrite, approved Oct 27 with conditions	done · Ritik · done Oct 29
A7	Merge trackA-nosol into local main; tests	done · Ritik · done Oct 30
Set A		
A18	Inside the fixed model	done · Ritik · done Nov 3
A29	Set A, an independent localization set	done · Ritik · done Oct 30
A32	Rank heads on set A for B1's head-subset variant	done · Ritik · done Oct 30
S7: validation loss		
A28	Training needs a baseline	done · Ritik · done Oct 28
B1: provenance scaling		
A30	B1, provenance-scaled attention at inference	done · Ritik · done Nov 3
B1R2	B1's deployable span against alpha = 1 on E2	planned · Ritik · due Nov 15
Thread 1 on Qwen3-8B		
A37	Thread 1 on a second model	done · Ritik · done Nov 1
Other		
E2	A second, larger held-out evaluation set	done · Ritik · done Nov 3

Track B: test widely

15 of 18 tasks done (83%). Owner: Arsha from Nov 6 (the work before, Ritik's).


A bar per task, by status; * = an inferred date (the Gantt sheet's Date basis says from what); dotted lines: gates and handoffs; shaded: the report and presentation windows.

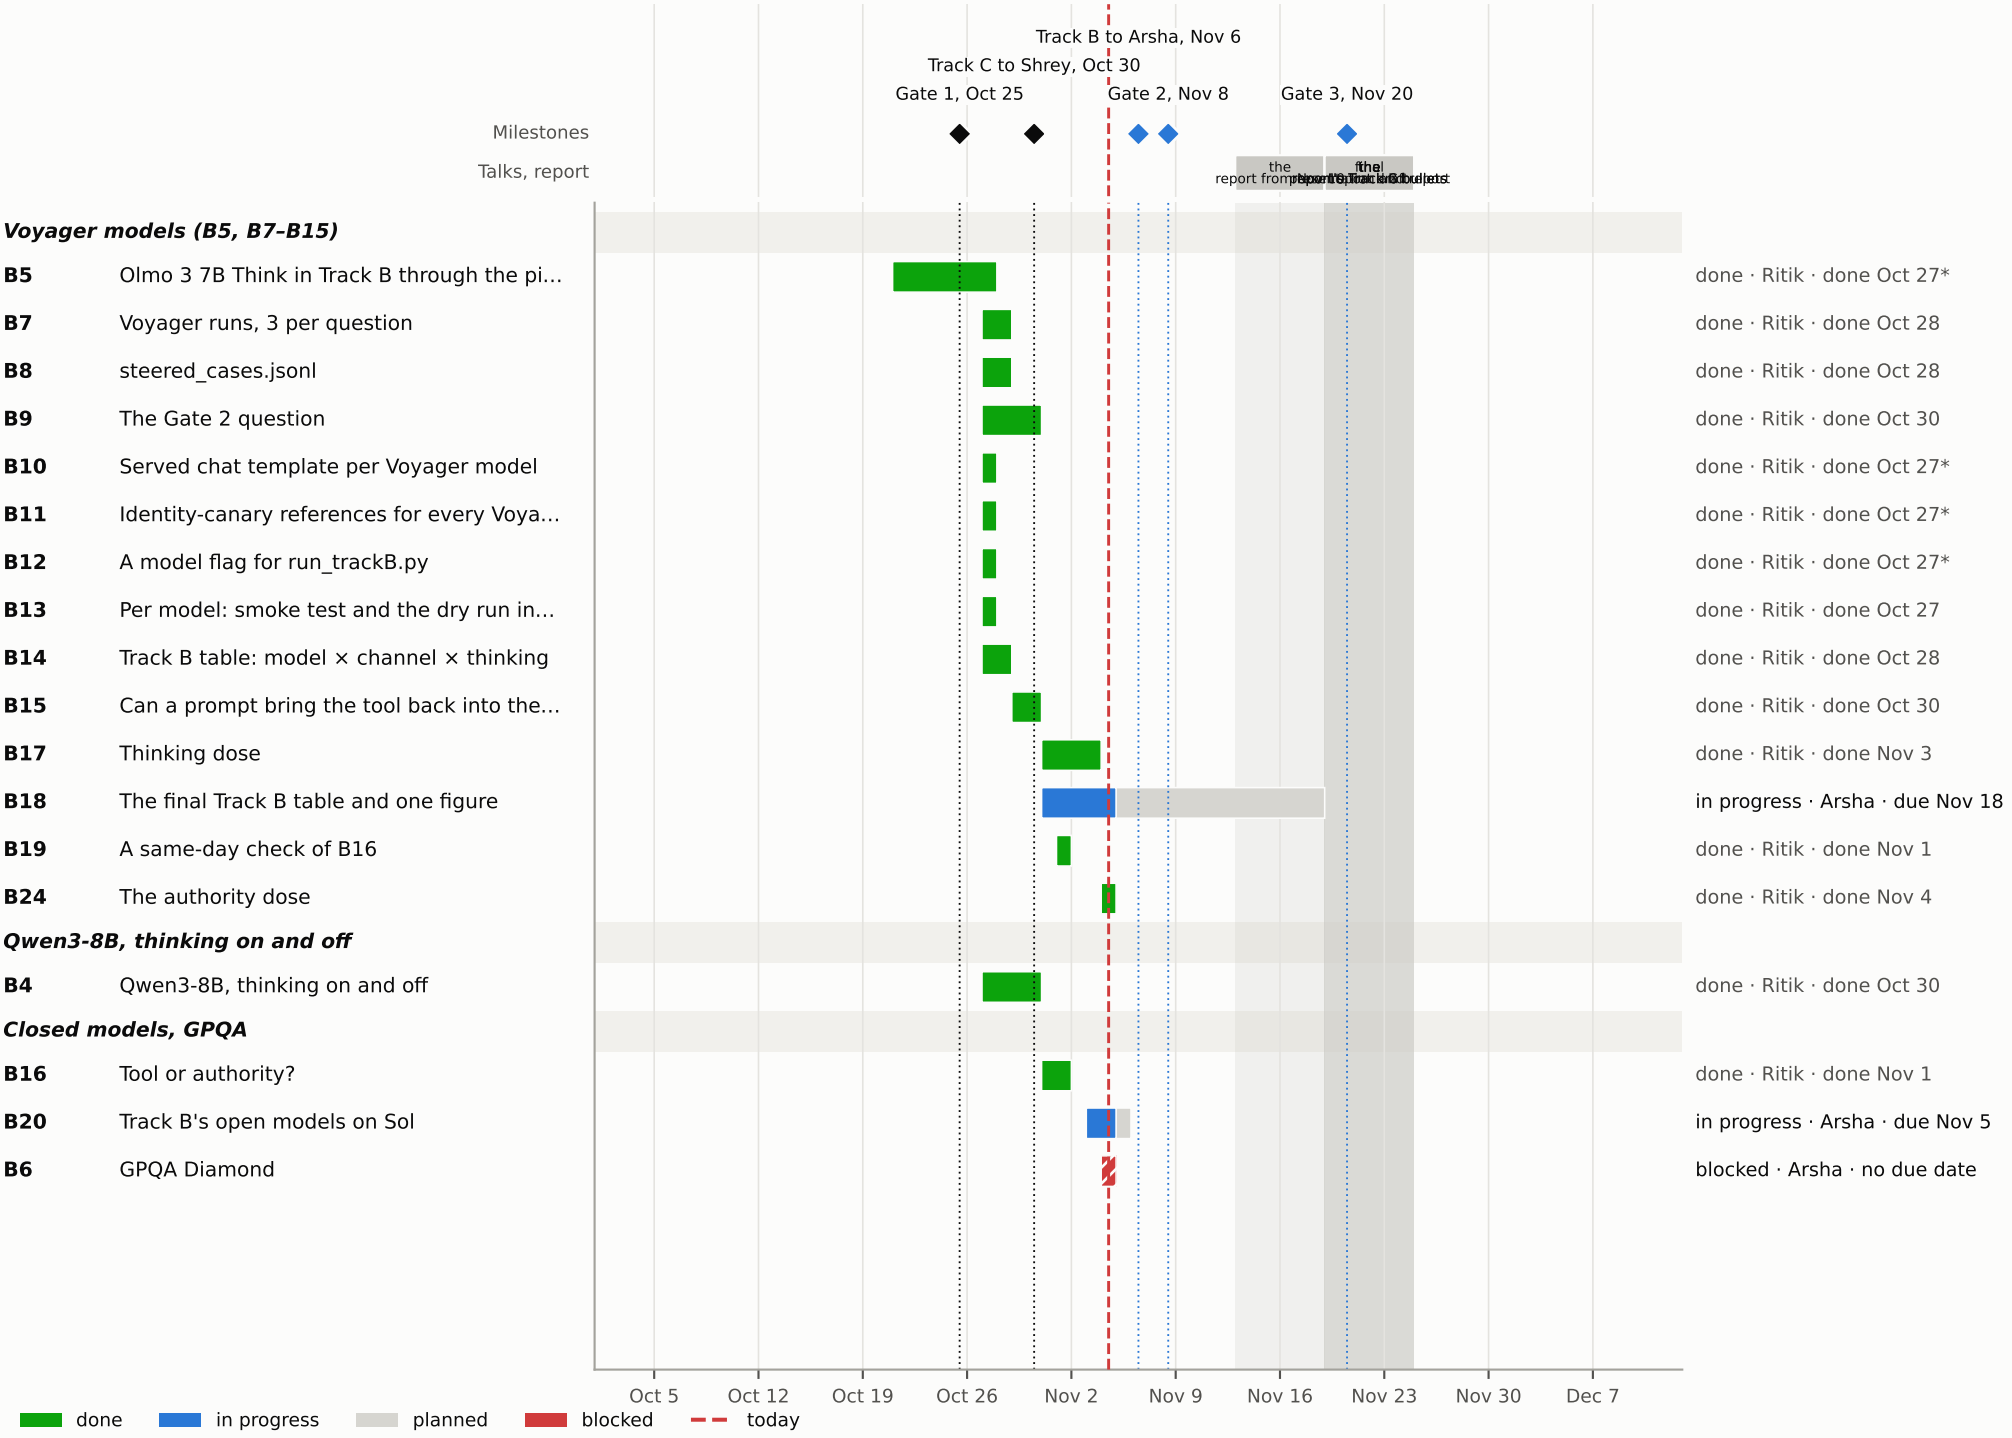

Track C: multi-agent pipeline

17 of 26 tasks done (65%). Owner: Shrey from Oct 30 (the work before, Ritik's).


A bar per task, by status; * = an inferred date (the Gantt sheet's Date basis says from what); dotted lines: gates and handoffs; shaded: the report and presentation windows.

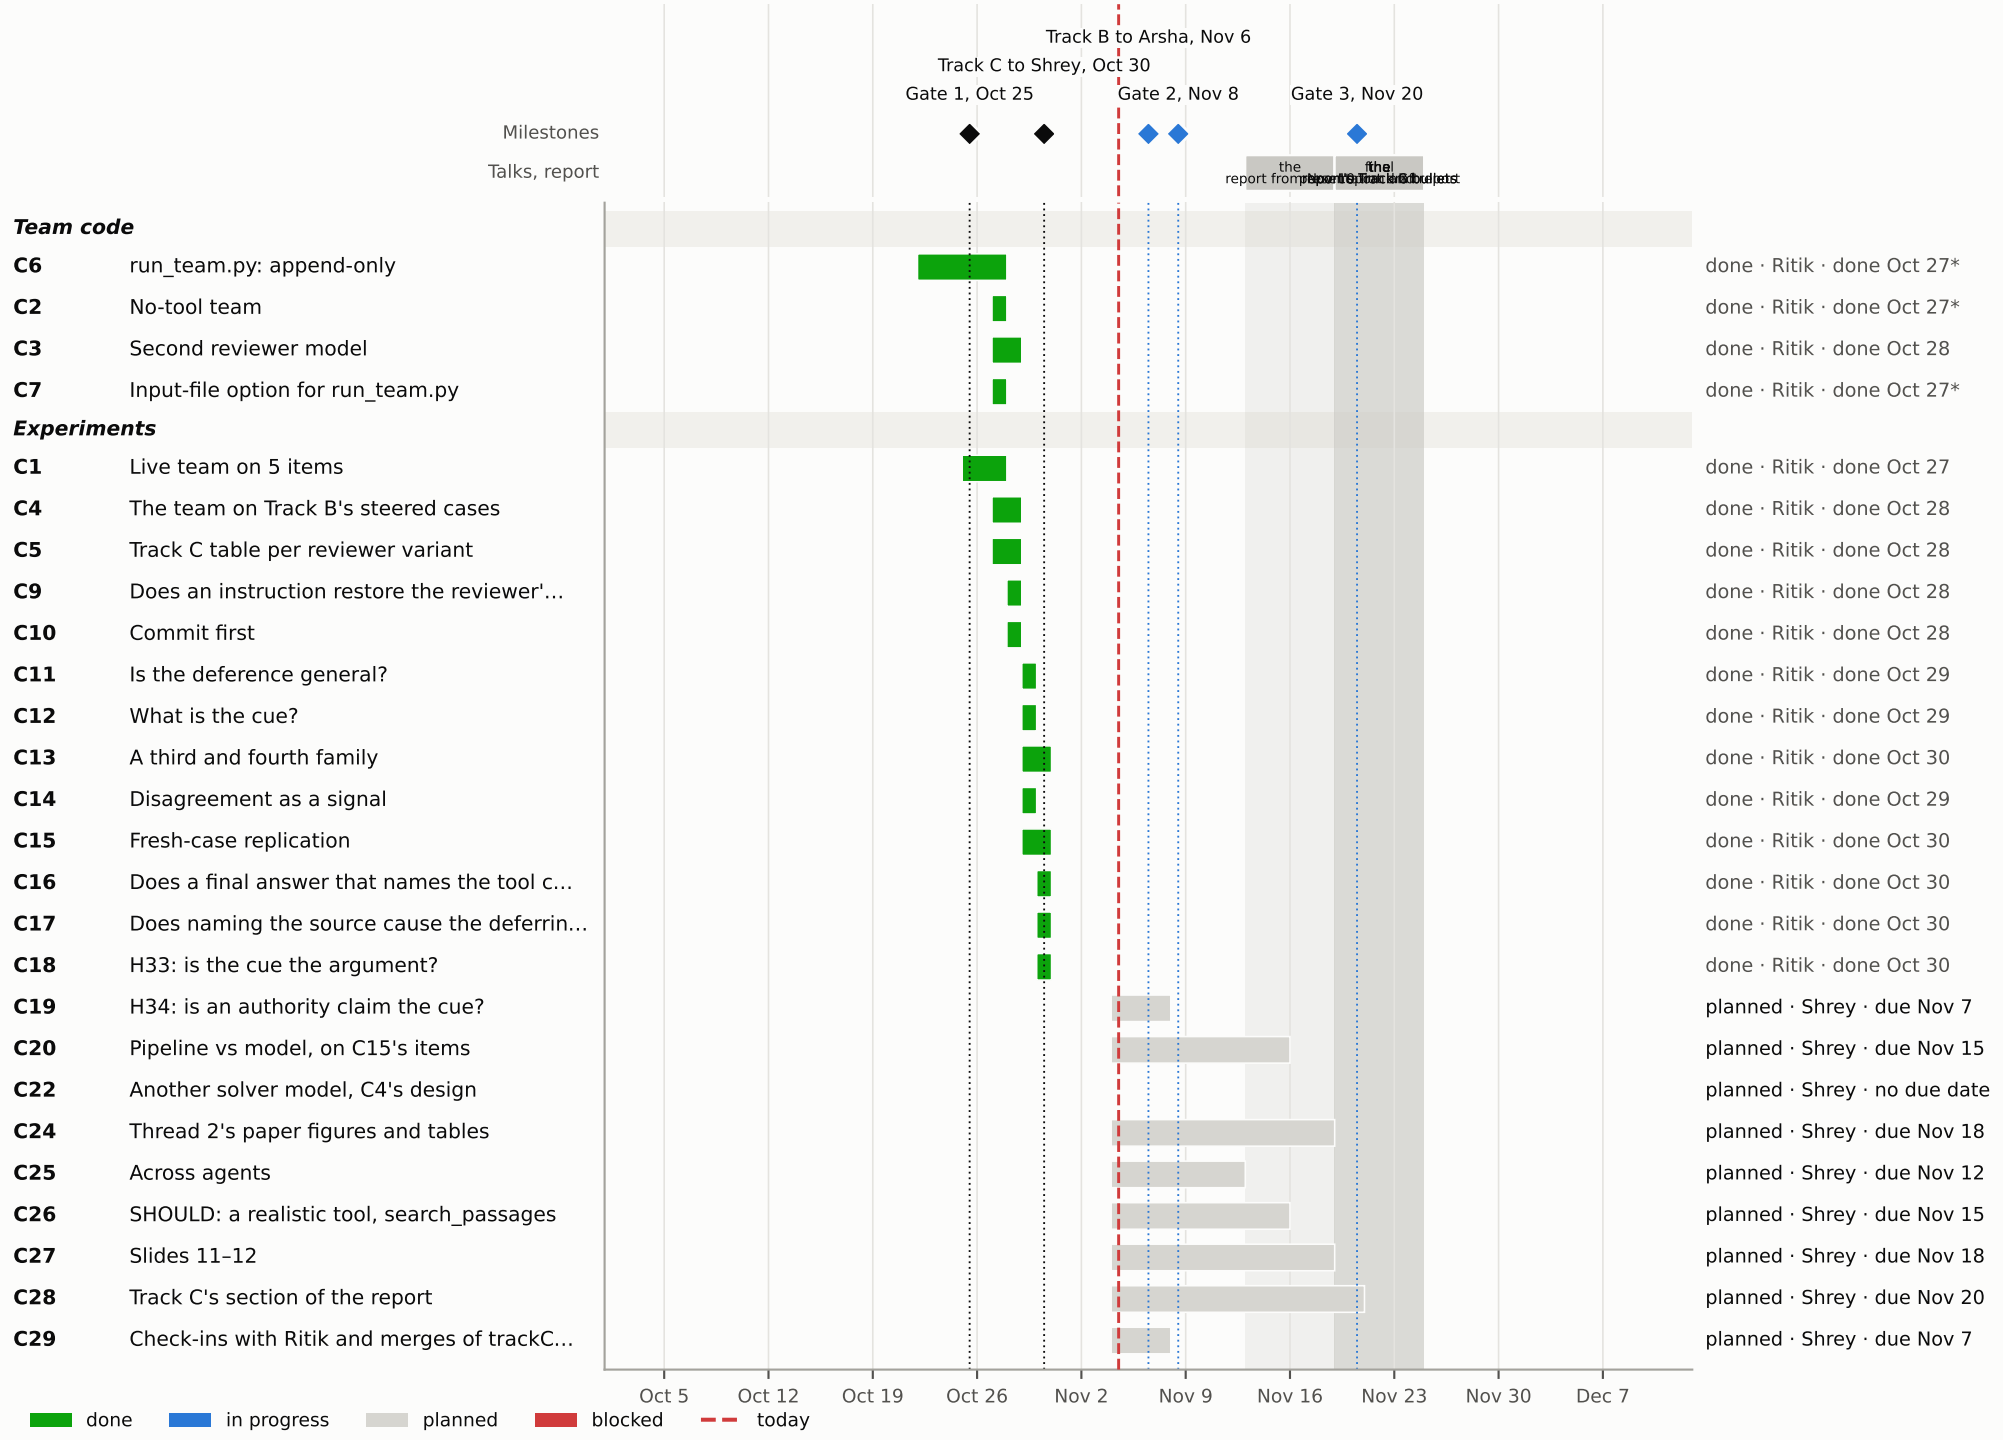

Labels

3 of 5 tasks done (60%). Owner: Ritik.

A bar per task, by status; * = an inferred date (the Gantt sheet's Date basis says from what); dotted lines: gates and handoffs; shaded: the report and presentation windows.

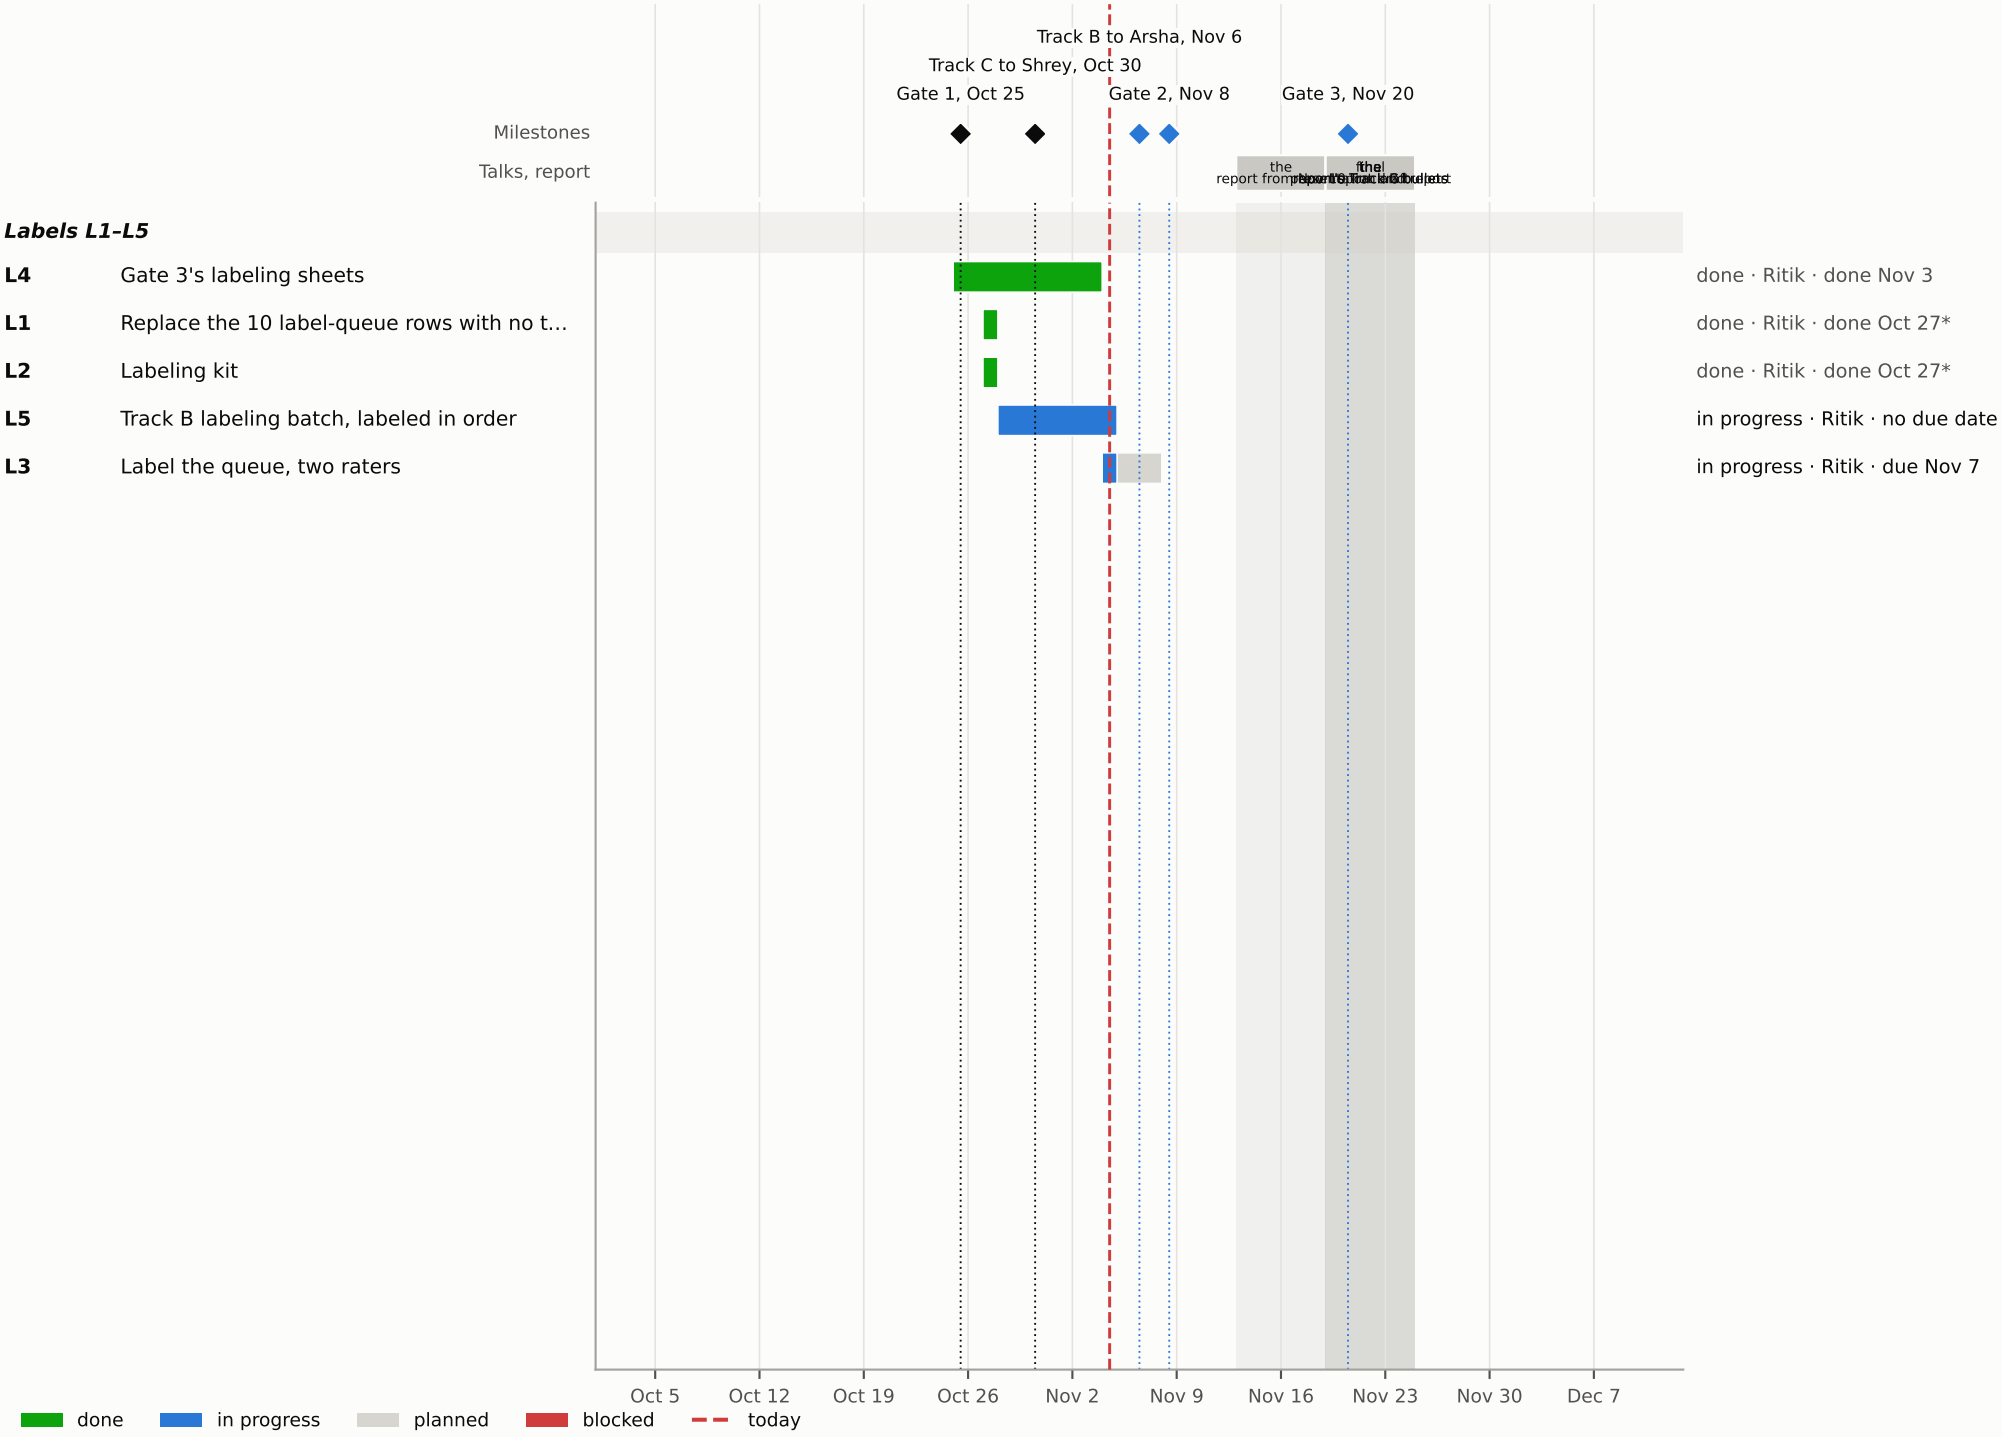

Repo, docs and handoff; Setup and the progress round

11 of 20 tasks done (55%). Owner: Ritik.

A bar per task, by status; * = an inferred date (the Gantt sheet's Date basis says from what); dotted lines: gates and handoffs; shaded: the report and presentation windows.

